



Board of Education Update

Congers Elementary School

Clarkstown Central School District

June 2, 2014

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Agenda

- Project Team
- Scope of Work
- Schedule
- Current Status

A large, solid red shape that curves from the bottom left towards the top right, filling the lower half of the page.

Project Team

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Project Team

- **CSArch**
Architecture, Interiors, Engineering, and Planning
 - Tom Ritzenthaler, Vice President
 - Robb Lafayette, Project Manager
- **Ryan-Biggs Associates**
Exterior Envelope and Structural Engineering
 - Jack Healy, Vice President
 - Neil Weisel, Senior Associate
- **Quality Environmental Solutions & Technologies**
Hazardous Materials Management
 - Paul Rodriguez, Director
- **Dente Engineering**
Geotechnical Engineering
 - Fred Dente, President



Scope

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Scope of Work

- Reconstruction of original 1927 South gymnasium wall
- Reconstruction of the original 1927 North and East walls
- Select ADA Accessibility upgrades at the main floor level
- Select window replacement in 1956 & 1970 additions
- Partial roof replacement

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Floor Plans

First Floor Plan



AGENDA

PROJECT TEAM


SCOPE

SCHEDULE

CURRENT STATUS

Floor Plans

Second Floor Plan

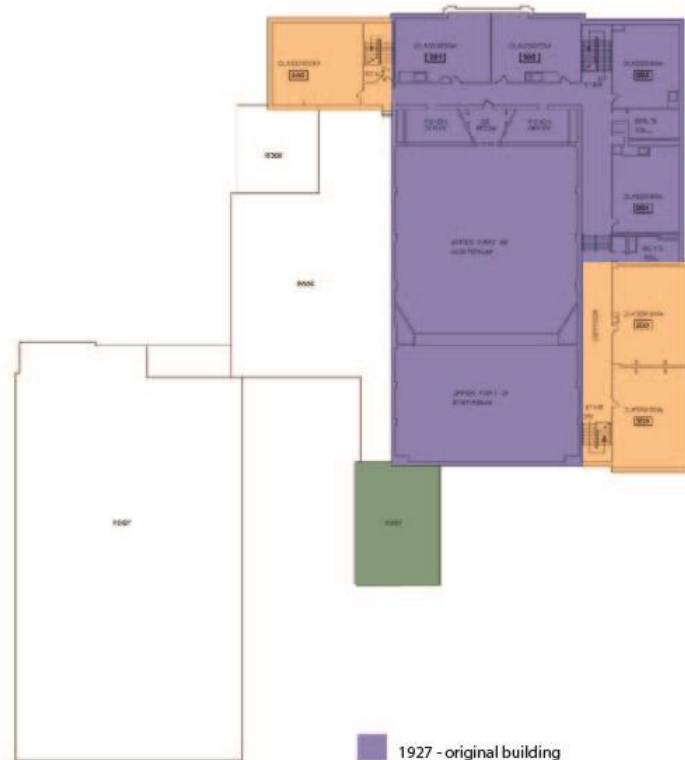

- 1927 - original building
- 1956 - classroom addition
- 1970 - library addition



Schedule

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Schedule

PHASE	2		0		1		4				2		0		1		5				
	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
Contract Documentation		■	■	■	●	■															
SED Review / Approval							■														
Bidding and Award							■	■													
Construction										■	■	■	■	■	■						
District Occupancy																		■	■		

- Contract Documentation
 - Schematic Design - Complete
 - Design Development - Complete
 - Construction Documentation – In Progress

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Schedule

- Schematic Design - Complete
 - Extensive field work
 - Develop base drawings
 - Conceptual design solutions
 - Completed April 2014



AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Schedule

- Design Development - Complete
 - Refinement of schematic design
 - Develop details
 - Material research
 - Hazardous materials field testing
 - Completed May 2014



AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Schedule

- Construction Documentation – In Progress
 - Finalize design
 - Completion of design package and submission to SED
 - On schedule to complete August 1, 2014



AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Schedule

PHASE	2		0		1		4				2		0		1		5				
	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
Contract Documentation		■	■	■	●	■															
SED Review / Approval							■														
Bidding and Award							■	■													
Construction										■	■	■	■	■	■	■					
District Occupancy																	■	■			

- SED Review and Approval
 - August 2014
- Bidding and Award
 - September - October 2014
- Construction
 - November 2014 – June 2015
- District Occupancy
 - July 2015 – August 2015

A large, solid red shape that curves from the bottom left towards the top right, filling the lower half of the page. The text 'Current Status' is positioned in the bottom right corner of this red area.

Current Status

AGENDA

PROJECT TEAM

SCOPE

SCHEDULE

CURRENT STATUS

Current Status

- Construction Documentation
 - In progress
 - Finalize design
 - Coordination with consultants
 - Geotechnical report pending
 - Further testing to confirm construction techniques
 - Completion of design package
 - Construction documents
 - Specifications
 - On schedule to complete on August 1, 2014
 - SED submission for review and approval

Thank you!
Questions?
