

**TO:** Anthony Valenti, Manager of Facilities  
**FROM:** Robert Lafayette, Project Manager  
**DATE:** February 13, 2015  
**Project:** Congers Elementary School Reconstruction  
**CSArch Project #:** 151-14-03

### **PROJECT SUMMARY**

The project is rapidly moving forward with the Construction phase.


### **CURRENT STATUS**


#### **Highlights**

- Project meetings take place every week. The next project meeting is scheduled for February 17.
- The Master Construction Schedule is attached.
- Cast stone, aluminum window, curtain wall, storefront, roof, and structural steel shop drawings as well as masonry submittals have been submitted and are currently under review.
- The RFI process is well under way now that areas have been exposed by demolition. **CSArch** is working with consultants to address these questions.
- During the week of February 9, the following tasks are progressing:
  - Installation of shoring and weather protection at the north end is complete.
  - Flooring abatement throughout the school is complete.
  - The piping abatement at stage/gym area is complete.
  - The plumbing contractor is working on rough plumbing of the toilet rooms with layout and material lists.
  - Boiler room plaster ceiling abatement is under way.
  - Structural demolition at the south wall, including slab removal, is in progress.

### **PROJECT REPORTING**

The next Project Status Report will be delivered on February 27, 2015.

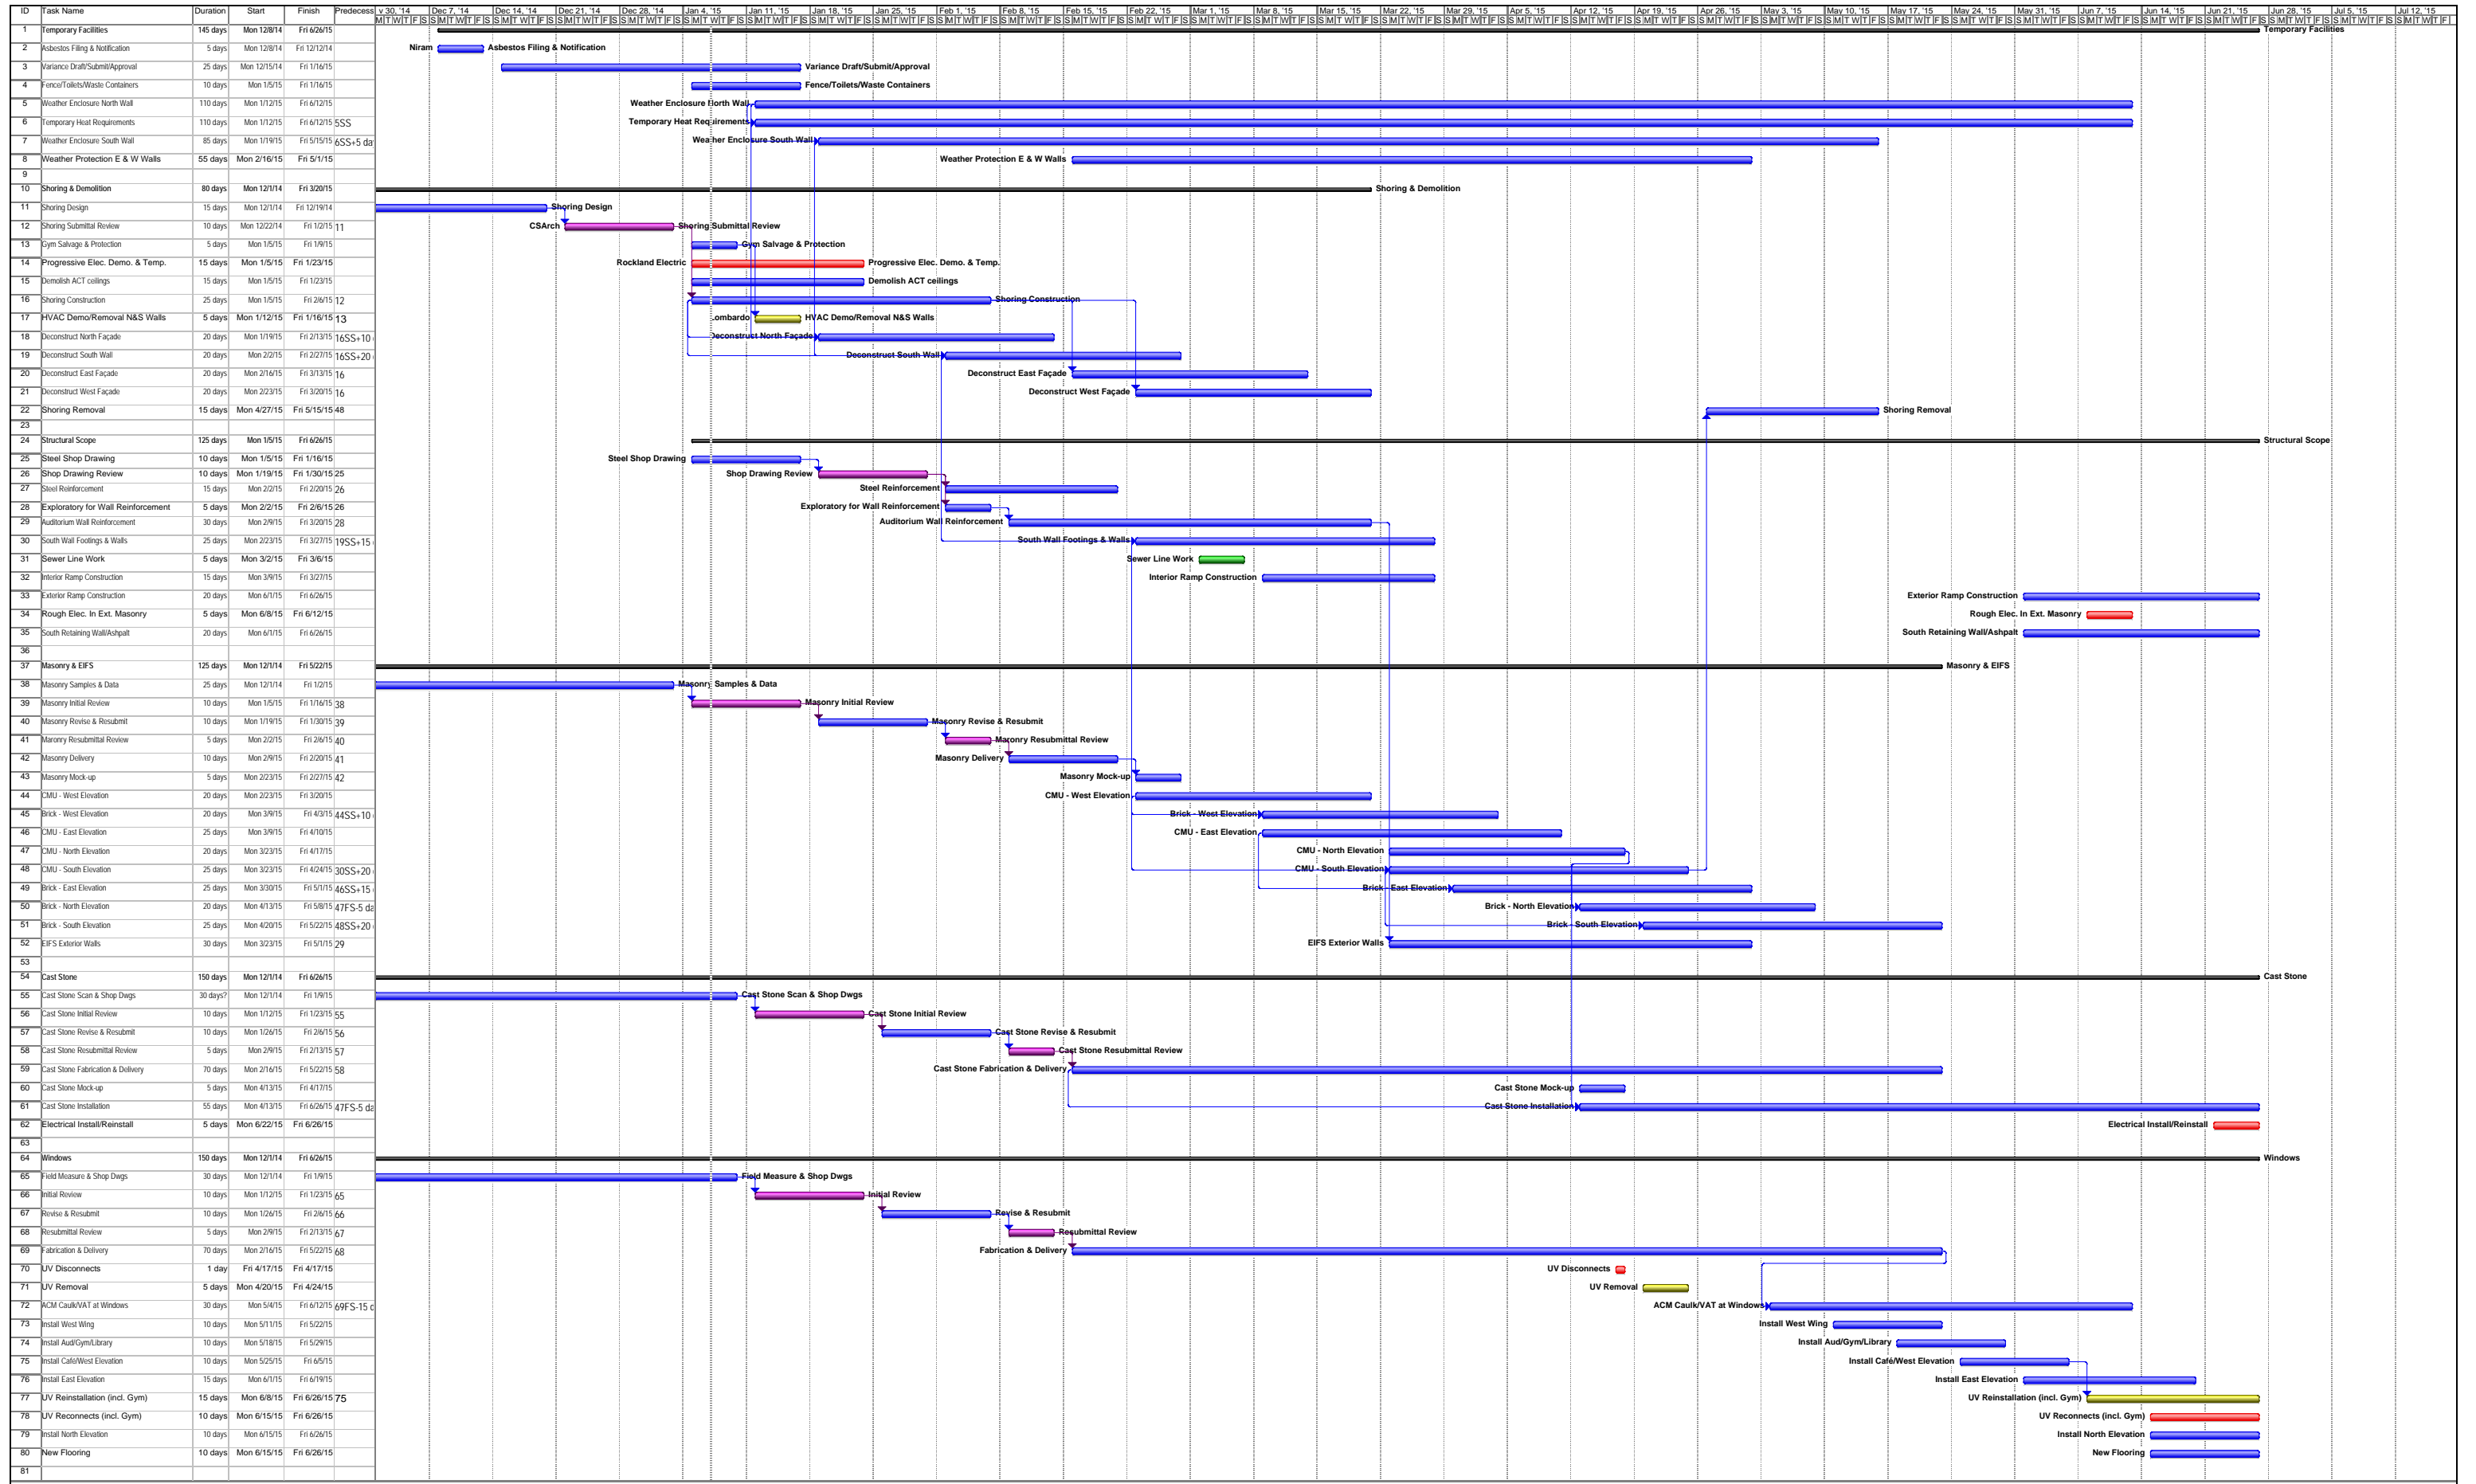

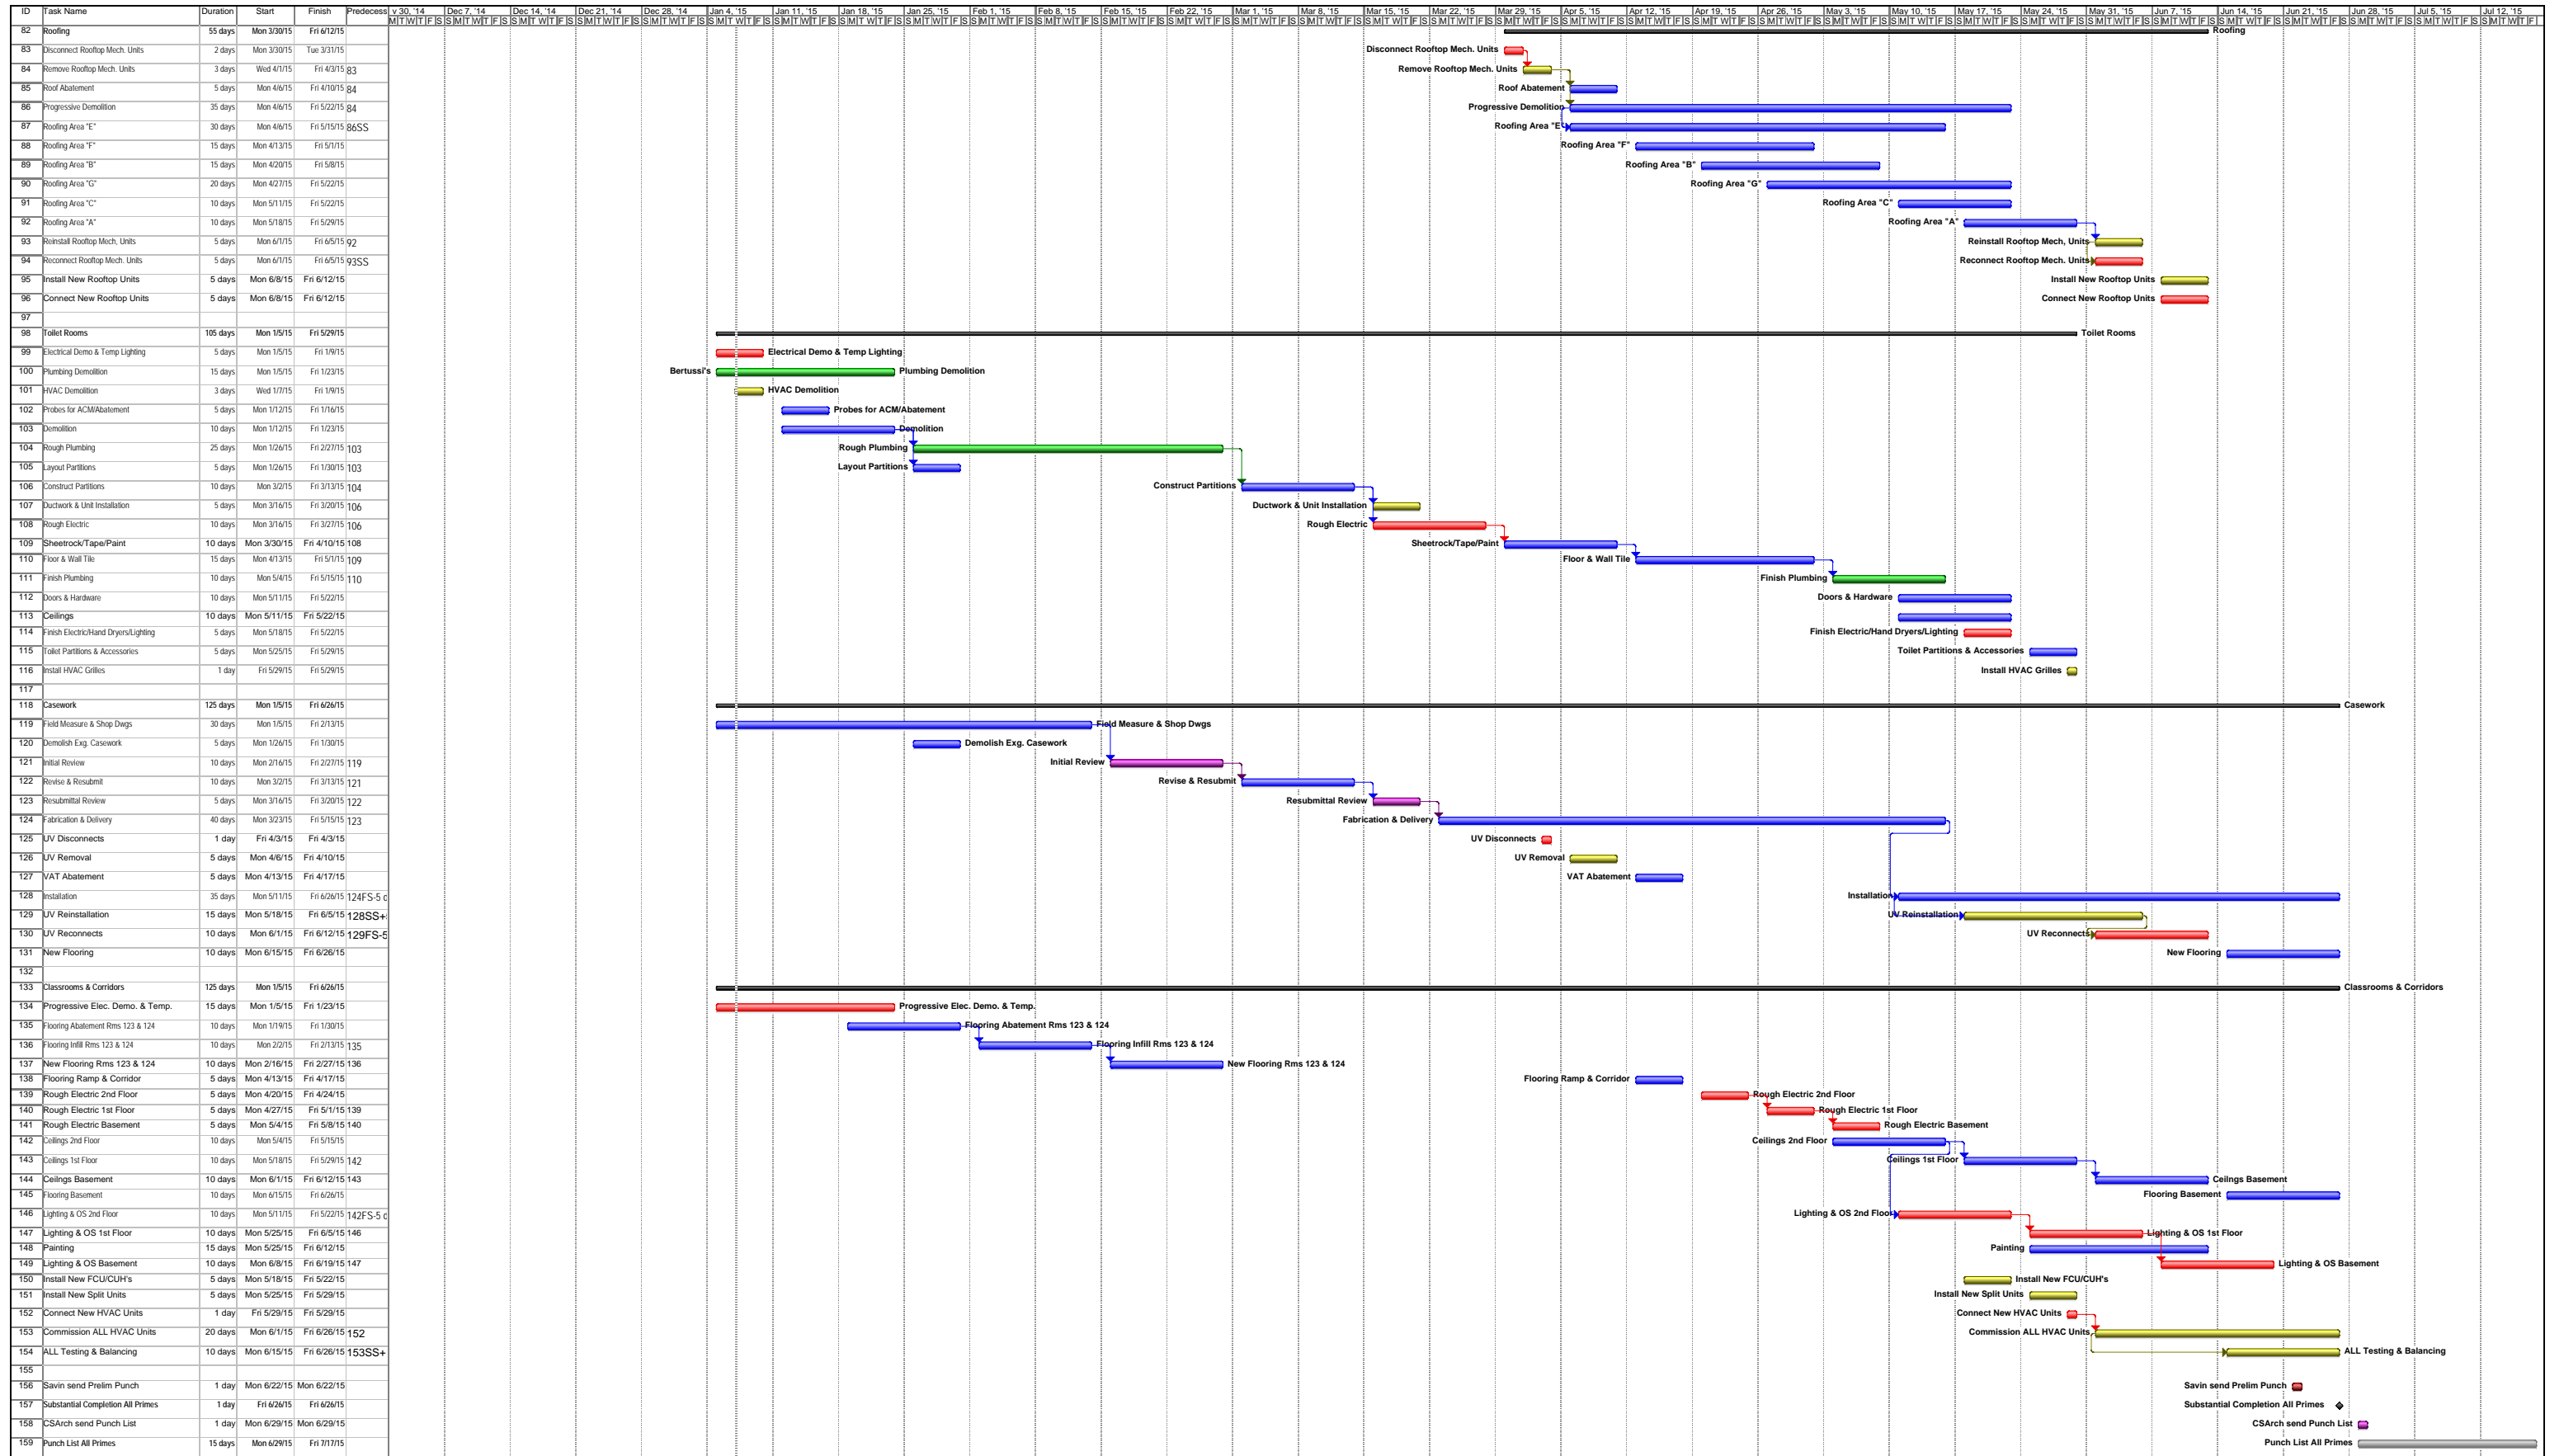

Project: Congers ES Master Schedule  
 Date: Wed 1/7/15

Task Split Progress Milestone Summary Project Summary External Tasks External Milestone Deadline
